



CONCRETE TRUCK WASH AREA NOT TO SCALE

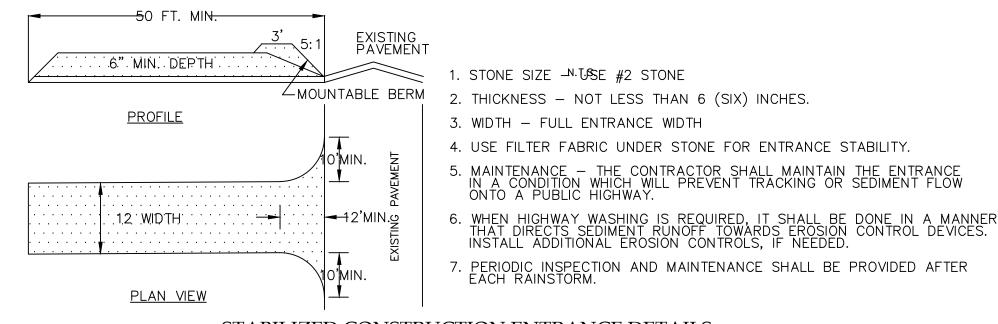

STABILIZED CONSTRUCTION ENTRANCE DETAILS NOT TO SCALE

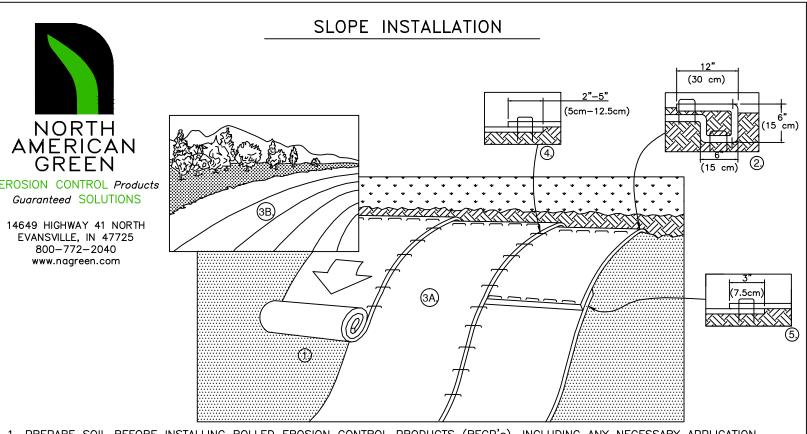

- PREPARE SOIL BEFORE INSTALLING ROLLED EROSION CONTROL PRODUCTS (RECP's), INCLUDING ANY NECESSARY APPLICATION NOTE: WHEN USING CELL-O-SEED DO NOT SEED PREPARED AREA. CELL-O-SEED MUST BE INSTALLED WITH PAPER SIDE DOWN.
- BEGIN AT THE TOP OF THE SLOPE BY ANCHORING THE RECP'S IN A 6" (15 CM) DEEP X 6" (15 CM) WIDE TRENCH WITH APPROXIMATELY 12" (30cm) OF RECP'S EXTENDED BEYOND THE UP-SLOPE PORTION OF THE TRENCH. ANCHOR THE RECP'S WITH A ROW OF STAPLES/STAKES APPROXIMATELY 12" (30 CM) APART IN THE BOTTOM OF THE TRENCH. BACKFILL AND COMPACT THE TRENCH AFTER STAPLING. APPLY SEED TO COMPACTED SOIL AND FOLD REMAINING 12" (30 CM) PORTION OF RECP'S BACK OVER SEED AND COMPACTED SOIL. SECURE RECP'S OVER COMPACTED SOIL WITH A ROW OF STAPLES/STAKES SPACED APPROXIMATELY 12" (30 CM) APART ACROSS THE WIDTH OF THE RECP's. 3. ROLL THE RECP'S (A.) DOWN OR (B.) HORIZONTALLY ACROSS THE SLOPE. RECP'S WILL UNROLL WITH APPROPRIATE SIDE
- AGAINST THE SOIL SURFACE. ALL RECP'S MUST BE SECURELY FASTENED TO SOIL SURFACE BY PLACING STAPLES/STAKES IN APPROPRIATE LOCATIONS AS SHOWN IN THE STAPLE PATTERN GUIDE. WHEN USING THE DOT SYSTEM™, STAPLES/STAKES SHOULD BE PLACED THROUGH EACH OF THE COLORED DOTS CORRESPONDING TO THE APPROPRIATE STAPLE PATTERN. 4. THE EDGES OF PARALLEL RECP's MUST BE STAPLED WITH APPROXIMATELY 2" - 5" (5 CM - 12.5 CM) OVERLAP DEPENDING
- 5. CONSECUTIVE RECP'S SPLICED DOWN THE SLOPE MUST BE PLACED END OVER END (SHINGLE STYLE) WITH AN APPROXIMATE 3" (7.5 CM) OVERLAP. STAPLE THROUGH OVERLAPPED AREA, APPROXIMATELY 12" (30 CM) APART ACROSS ENTIRE

*IN LOOSE SOIL CONDITIONS, THE USE OF STAPLE OR STAKE LENGTHS GREATER THAN 6" (15 CM) MAY BE NECESSARY TO

TOWN OF CANANDAIGUA STANDARD NOTES

- 1. ALL IMPROVEMENTS SHALL BE IN ACCORDANCE WITH THE MOST RECENT STANDARDS AND SPECIFICATIONS OF THE TOWN OF CANANDAIGUA AND THE APPROPRIATE WATER / SEWER AGENCIES, UNLESS OTHERWISE NOTED.
- 2.SEQUENCE THE CONTRACTOR SHALL INSTALL EROSION CONTROL MEASURES IN THE FOLLOWING
- SEQUENCE UNLESS AUTHORIZED OTHERWISE AT THE PRE- CONSTRUCTION MEETING: • INSTALL PERIMETER SEDIMENT CONTROLS, (I.E. EROSION FENCING).
- INSTALL STABILIZED CONSTRUCTION ENTRANCE.
- PROTECT VEGETATION TO REMAIN.
- CLEAR GRUB AND CONSTRUCT DIVERSIONARY SWALES AND SEDIMENT BASINS.
- COMPLETE CLEARING AND GRUBBING OPERATION. • PLACE EROSION CONTROL MEASURES AROUND TOPSOIL STOCKPILES AND STRIP TOPSOIL LOCATIONS.
- CONSTRUCT SWALES AND SILTATION DEVICES AS EARTHWORK OPERATIONS PROGRESS. • MAINTAIN EROSION CONTROL MEASURES AND PLACE ADDITIONAL MEASURES AS EARTHWORK AND
- UNDERGROUND UTILITIES ARE CONSTRUCTED. • RESTORE AREAS AS DEFINED BY CONTRACT DOCUMENTS.
- REMOVE EROSION CONTROL MEASURES AS AREAS ARE REESTABLISHED WITH GROUND COVER.
- IF SITE PREPARATIONS OCCUR BETWEEN SEPTEMBER 1 AND MARCH 31, ADDITIONAL EROSION CONTROLS MUST BE TAKEN INCLUDING REDUCING THE SIZE OF DISTURBANCE AREA AND PLACING HEAVY STRAW MULCH WHERE PRACTICAL.
- 3. PLANS SHOULD INCLUDE RE-SEEDING INSTRUCTIONS INCLUDING MATERIALS AND A TIMETABLE FOR
- SEED ALL CUT AND FILL, TOPSOIL PILES AND PONDS WITHIN SEVEN (7) DAYS AFTER COMPLETION.

• TEMPORARY SEEDING OF DISTURBED AREAS SHALL BE PROVIDED AS FOLLOWS:

THE SURFACE TWO INCHES OF SOIL SHOULD BE LOOSENED BY DISKING, RAKING, OR BACK-BLADING WITH A BULLDOZER. IMMEDIATELY FERTILIZE WITH 300 POUNDS PER ACRE (OR 7 POUNDS PER 1,000 SQUARE FEET) OF 10-10-10 FERTILIZER. IMMEDIATELY SEED WITH THE FOLLOWING MIX:

LBS/ACRE LBS/1,000 SQ. ACRES SPRING/SUMMER/EARLY FALL ANNUAL RYE GRASS 30 PERENNIAL RYEGRASS 30 0.7 LATE FALL/EARLY WINTER

CEREAL RYE

SEED SHOULD HAVE A GERMINATION RATE OF AT LEAST 85 PERCENT AND MINIMAL

DISTURBED AREAS SHALL BE STABILIZED USING PERMANENT LAWN SEEDING MIX UPON COMPLETION OF GRADING AND CONSTRUCTION:

2.5

LBS/ACRELBS/1,000 SQ. ACRE BIRDSFOOT TREFOIL OR COMMON WHITE CLOVER 8 OR 8 0.20 OR 0.20 TALL FESCUE

REDTOP OR RYEGRASS (PERENNIAL) 2 OR 5 0.05 OR 0.10 SEEDING RATE: 6.0 POUNDS PER 1,000 SQUARE FEET

MULCH: STRAW OR WOOD FIBER MULCH USED WITH HYRDO SEEDING METHOD AT TWO TONS PER ACRE WITH TRACKIFIER. STARTING FERTILIZER: 5:10:10 AT 20 POUNDS PER 1,000 SQUARE FEET.

- FOR FALL OR EARLY WINTER, SEED WITH CERTIFIED □AROOSTOCK□ WINTER RYE (CEREAL RYE) AT 100 POUNDS PER ACRE.
- PERMANENT STABILIZATION FOR STEEP SLOPES GREATER THAN 3:1 SHALL INCLUDE JUTE MESH BLANKET AND CROWN VETCH SEED WITH PERENNIAL RYEGRASS.
- 4.THE CONTRACTOR SHALL LOCATE, MARK, SAFEGUARD AND PRESERVE ALL SURVEY CONTROL MONUMENTS AND RIGHT-OF-WAY MONUMENT IN THE AREAS OF CONSTRUCTION.
- 5.EXISTING UNDERGROUND UTILITIES SHOWN HEREIN WERE PLOTTED FROM FIELD LOCATIONS AND /OR UTILITY COMPANY RECORD PLANS. PRIOR TO ANY CONSTRUCTION, THE CONTRACTOR SHALL CALL THE DIG SAFELY NEW YORK (UFPO) HOTLINE AT 1-800-962-7962 FOR STAKEOUT OF EXISTING UTILITIES. THE CONTRACTOR SHALL DETERMINE EXACT LOCATION AND EVALUATION OF UNDERGROUND UTILITIES BEFORE COMMENCING CONSTRUCTION. CONTRACTOR SHALL MAKE EXPLORATION EXCAVATIONS TO LOCATE EXISTING UNDERGROUND FACILITIES SUFFICIENTLY AHEAD OF CONSTRUCTION TO PERMIT REVISIONS AS REQUIRED TO MEET THE EXISTING CONDITIONS.
- 6.DUST SHALL BE CONTROLLED DURING CONSTRUCTION BY THE CONTRACTOR TO MINIMIZE EFFECT ON THE ADJACENT PROPERTIES. THE CONTRACTOR SHALL IMPLEMENT DUST CONTROL MEASURES AS NEEDED AND/ OR DIRECTED BY THE TOWN OF CANANDAIGUA.
- 7. THE OWNER'S CONTRACTOR SHALL BE RESPONSIBLE FOR THE ESTABLISHMENT, MAINTENANCE, CLEANING, REPAIR AND REPLACEMENT OF EROSION CONTROL MEASURES DURING SITE CONSTRUCTION.
- 8.ROOF LEADERS SHALL BE CONNECTED TO STORM SEWERS.
- 9.NO SITE PREPARATION SHALL COMMENCE UNTIL A VISUAL INSPECTION BY THE TOWN OF CANANDAIGUA CONFIRMS THE INSTALLATION OF PERIMETER SEDIMENT CONTROLS.
- 10. ANY ADDITIONAL EROSION OR SEDIMENT CONTROL DEEMED NECESSARY BY THE TOWN OR A REPRESENTATIVE THEREOF SHALL BE PROVIDED BY THE OWNER.
- 11. SEDIMENT CONTROL MEASURES ARE TO BE ESTABLISHED PRIOR TO COMMENCING EARTHWORK. SEDIMENT CONTROL MEASURES ARE TO BE MAINTAINED BY THE CONTRACTOR UNTIL UPSTREAM GROUND COVER HAS BEEN ESTABLISHED AND REMOVAL IS APPROVED BY THE TOWN OF CANANDAIGUA.
- 12. THE CONTRACTOR IS RESPONSIBLE FOR MAINTAINING, REPLACING AND SUBSEQUENTLY REMOVING TEMPORARY EROSION & SEDIMENT CONTROL DEVICES.
- 13. THE CONTRACTOR SHALL BE RESPONSIBLE FOR CLEANING ADJOINING PROPERTIES, ROADWAYS, DRAINAGE WAYS AND SINKS OF SILT ACCUMULATION AS NEEDED AND AS DETERMINED/ REQUESTED BY THE TOWN OF CANANDAIGUA.
- 14. ANY FINAL GRADE DEVIATIONS OF HOUSE PAD ELEVATIONS MORE THAN 12 INCHES SHALL BE APPROVED BY THE PLANNING BOARD.


FINAL SITE PLAN APPROVAL

PLANNING BOARD CHAIRPERSON DATE TOWN HIGHWAY & WATER SUPERINTENDENT DATE TOWN ENGINEER DATE

NO BUILDING PERMIT MAY BE ISSUED UNTIL FINAL SITE PLAN APPROVAL HAS BEEN GRANTED AND THE FINAL SITE PLAN SIGNED BY THE PLANNING BOARD CHAIRPERSON.

FOR PERMITTING ONLY







OF WEW.		kevisions			1 N
VENEZIA VO	NO.	Date	Description	Ву	
1 2 2 E	1	3/17/16	Town Comments	EVJ	
2 m					
08676A					
STORY OF THE PARTY					
317 16					
1					ŧ

Site Plan Prepared For: Property Owner Corey Westbrook

Drawing Title:

4118 Onnalinda Drive Canandaigua, NY 14424

Corey Westbrook Showing Land

EROSION CONTROL DETAILS

Onnalinda Drive Town of Canandaigua

T.m. # 113.17-1-31.0 AS NOTED 3/10/16

File# 15230 **—**

Sheet 3 of 3

■ 5120 Laura Lane **——** Canandaigua New York, 14424

Rocco A. Venezia, P.L.S.

State of New York County of Ontario ____ (585)396-3267 _____ Fax. No. (585) 396-0131 _____ E-mail rocco@veneziasurvey.com ___ www.veneziasurvey.com
